


	OCCUPATIONAL HEALTH & SAFETY MANAGEMENT SYSTEM		Document Number: DIMO-LTD-CL-03
	CHECKLIST		Issue: 00
	BOOM TRUCK/CRANE		Issue Date: 1st January 2021

Project		Date of Inspection	
Contractor's Name		Frequency	
Date of first deployment		Checked by	

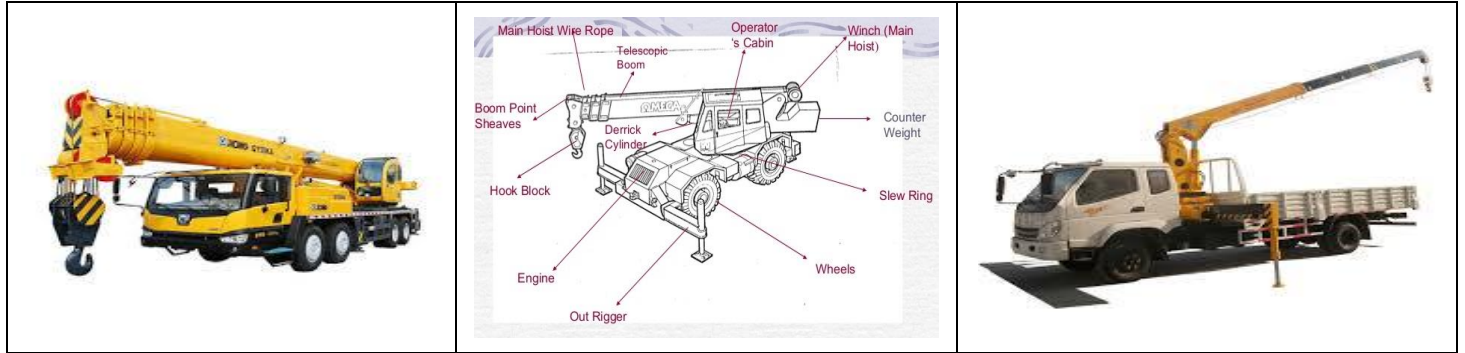

S/N	INSPECTION POINTS	YES	NO	N/A	REMARKS
01	Crane hook latch is available and in good condition				
02	Hoist limit switch is available				
03	SWL marked in crane.				
04	Wire rope and slings free from tolerable damage				
05	No oil leak in hydraulic parts				
06	Front and reverse horn is working				
07	Boom structure is in good condition				
08	Electrical system, running lights, brake lights and turn signals are working.				
09	Operator's Heavy vehicle license available				
10	Tires in good condition. (have no cuts, bulges, worn treads or steel belts showing)				
11	Side view and back view mirrors are available.				
12	Automatic safe load indicator is available and working in good condition (ASLI).				
13	Valid third party inspection certificate is available				

Overall Observation	Accepted: Yes No	Remarks:
Removal of Equipment/Machine (If not acceptable)	Date:	Remarks:
If Corrective/Preventive action taken to rectify	Date:	Remarks:

Checked by	Name	Date	Signature
Contractor's Supervisor			
EHS Officer			
Site In charge/Manager			
