


	OCCUPATIONAL HEALTH & SAFETY MANAGEMENT SYSTEM		Document Number: DIMO-LTD-CL-09
	CHECKLIST		Issue: 00
	EXCAVATOR		Issue Date: 1 st January 2021

Project		Date of Inspection	
Contractors Name		Frequency	
Date of first deployment		Checked by	
Type		Serial No	

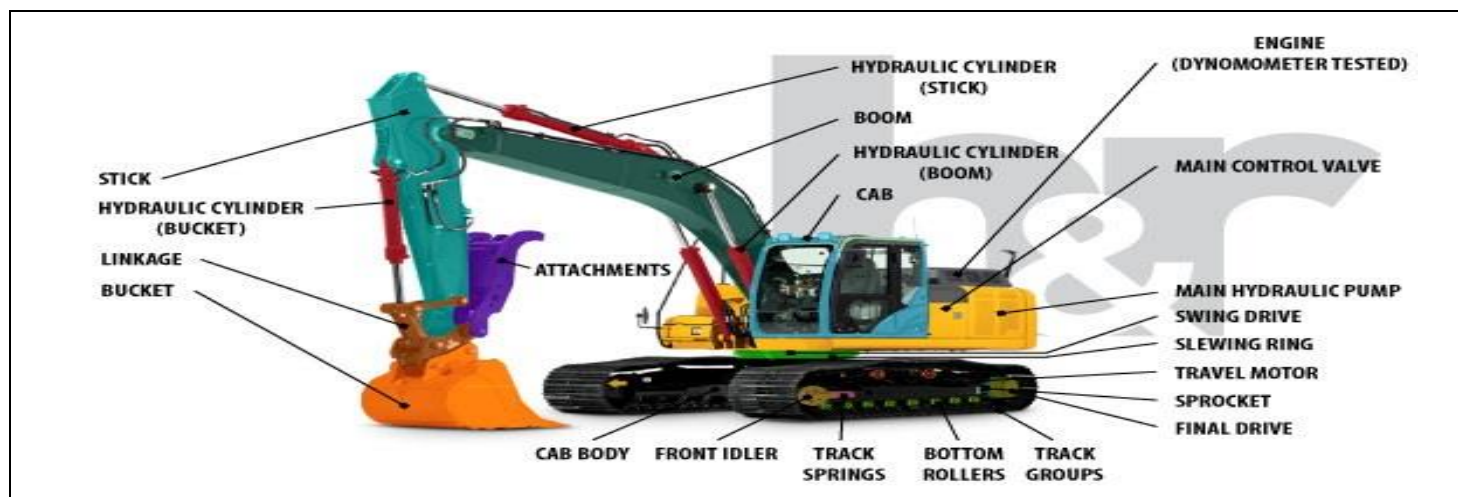

S/N	INSPECTION POINTS	YES	NO	N/A	REMARKS
01	Structure beam is free from damage, cut or crack.				
02	No any diesel, oil and grease spillage/leakage.				
03	No any loose bolts in bucket teeth or connecting pins.				
04	Rear view mirror available.				
05	Front & reverse horn is in working condition.				
06	Head & tail lamps are available and in working condition.				
07	Roller-crawler is free from damage or cracks.				
08	Swing area has been barricaded and warning signs has been provided.				
09	Operator is competent (Certified) and heavy vehicle license is available.				
10	Third party inspection certificate is available for the machine				

Overall Observation	Accepted: Yes No	Remarks:
Removal of Equipment/Machine (If not acceptable)	Date:	Remarks:
If Corrective/Preventive action taken to rectify	Date:	Remarks:

Checked by	Name	Date	Signature
Contractor's Supervisor			
EHS Officer			
Site In charge/Manager			
